



Overview of progress in the NIVA Project

Sander Janssen (WR, coordinator) with contributions from many




This project has received funding from the European Union's Horizon 2020 research and innovation programme under grant agreement No. 842009

NIVA Progress from Copenhagen, November 2019 to May 2020

NEW ACES VISION IN ACTION

NEW IACS VISION in ACTION - NIVA

- H2020 Innovation Action
- Proposal in response to [call](#): Digital solutions and e-tools to modernise the CAP
- Consortium
 - lead = WUR
 - 9 paying agencies (NL-DK-SP-IT-FR-GR-EE-LT-IR)
 - technical partners, total 27 partners

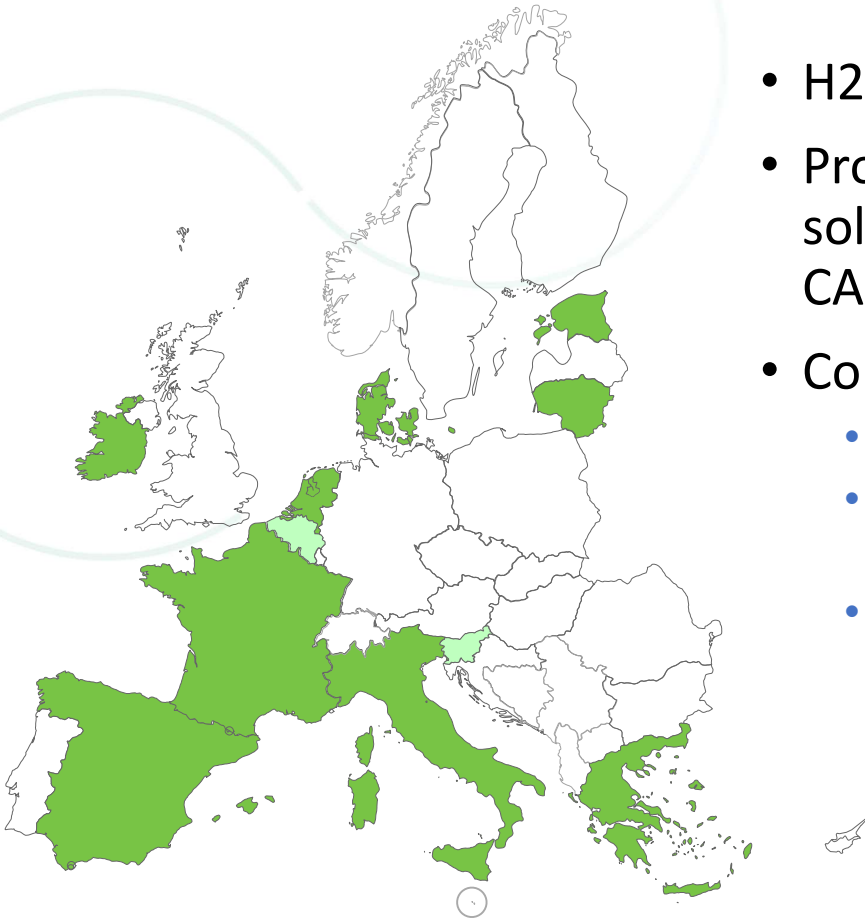


three main challenges:

- Absorbing innovations to simplify the CAP governance;
- Reducing socio-economic and administrative burden to farmers;
- Reducing the gap between IACS data use and potential broader uses.

While: the European Commission proposes a more flexible system, simplifying and modernising the way the CAP works. The policy will shift the emphasis from compliance and rules towards results and performance.

Pilots at the core

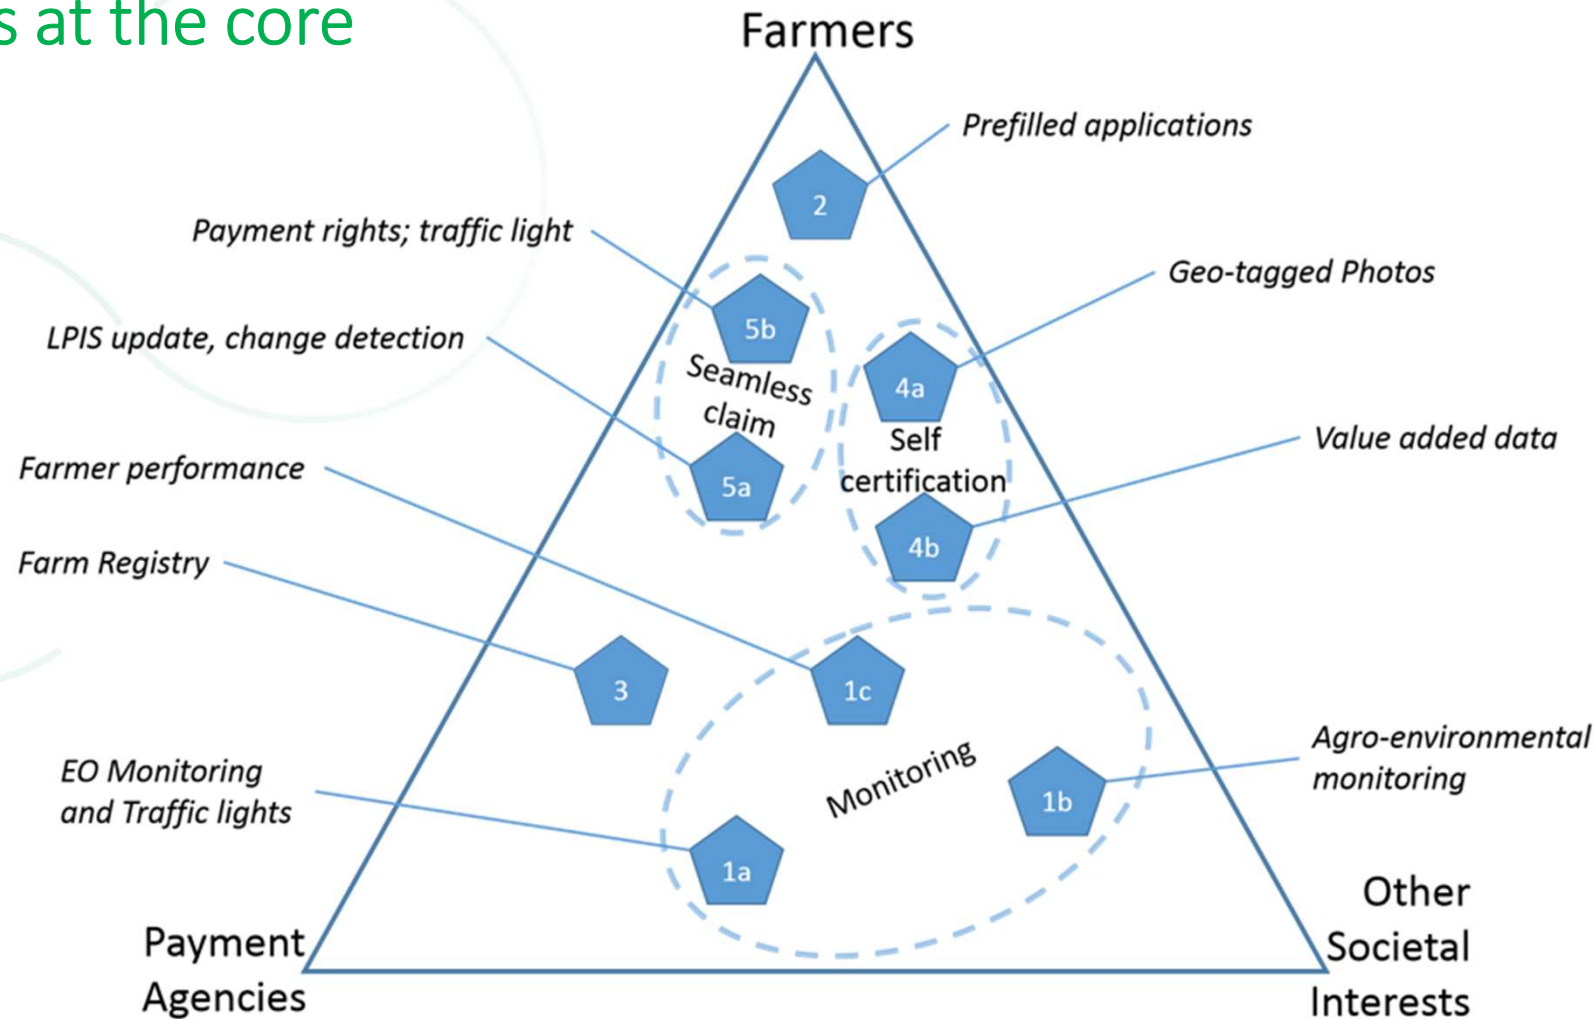


Pilots and testing partners

Use Case Group	Use Case id	Use Case title	Lead MS (PA)	Testing PAs
Monitoring	UC1a	Earth Observation Monitoring and Traffic Lights	Greece (OPEKEPE)	DAFM, ASP, ARIB, AGEA
	UC1b	Agro-environmental monitoring	France (ASP)	RVO, DAA, FEAGA (ITACYL)
	UC1c	Farmer Performance	Estonia (ARIB)	AGEA
Prefilled application	UC2	Prefilled application, GSAA/Land link	Lithuania (NPA)	FEAGA
Farm Registry	UC3	Farm Registry	Spain (FEAGA)	CAPDER
Self-Certification	UC4a	Geotagged photos	Ireland (DAFM)	NPA, ARIB, AGEA, OPEKEPE
	UC4b	Machine data in GSAA as added value data	The Netherlands (RVO)	DAA, FEAGA (ITACYL), OPEKEPE
Seamless Claim	UC5a	LPIS: Update & Change detection	Denmark (DAA)	ASP, FEAGA
	UC5b	Scheme Eligibility and Payment Eligibility: Click-and-Pay.	Italy (AGEA)	



Milestones



Milestone	Title	Due Date
M1	Project start	1 (June 2019)
M2	Inception	6 (Nov 2019)
M3	Single MS pilot start	12 (May 2020)
M4	Start of multiple MS pilot	18 (Nov 2020)
M5	Demonstration review	24 (May 2021)
M6	Roadmap and demonstration review	30 (Nov 2021)
M7	Final delivery (results conference)	36 (May 2022)

What was achieved by Copenhagen, nov. 2019?

1. Project started, really fast
2. New NIVA participants across partners
3. Internal means of communication established!
4. Decision making bodies activated

From exploratory to executive

- Around M6 (Copenhagen), many discussions: how to do this? What should be the scope? How can we collaborate?
- Many decisions taken, scope of many activities determined
 - Ucs in WP2 are all developing, some with dependencies
 - Common Components in WP4 have determined role
 - Questionnaires in WP3 finalised and determining directions for interventions



- Execution as a priority leading to the Milestones of Single Memberstate Pilot
- Next step of testing across Member States
- Synergy of activities over WPs

From in-ward organization to outwardly visible

- In M6 (Copenhagen), first Stakeholder Forum on *Implementation of CbM*
- Stakeholder awareness of NIVA existence
- Requests for more cooperation, and availability of NIVA resources (source code, lessons learned) from stakeholders
- Experiments with outward facing products (website, Policy Brief, Twitter)



- Further increase reach of NIVA products: more website visits, etc
- Set up rules-of-engagement with outside stakeholders
- Develop more short communications such as Policy Briefs

NIVA & COVID pandemic: impacts and mitigation measures


NEWACES VISION IN ACTION

COVID 19 Pandemic in general

- In-person meetings are not possible, hence visiting farmers or in-person stakeholder meeting
- Partner and stakeholder organizations need to switch to home working
- Potentially other priorities within partner organizations for the short term



- Loss of focus in the short term
- Loss of ad-hoc coffee break type of discussions
- More difficult to reach stakeholders not yet aware of NIVA

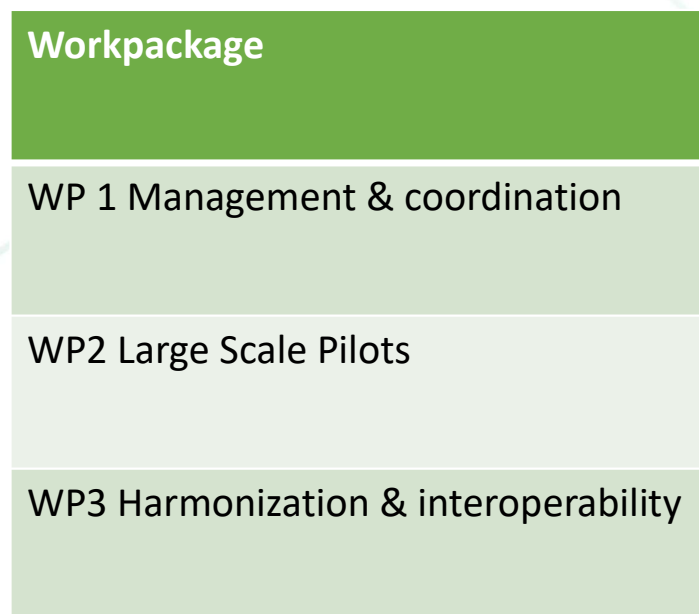

Workpackage	Impact	Mitigation measures
WP 1 Management & coordination	Minimum; mostly on implementation of innovation management	Rescheduling physical meetings to virtual meetings
WP2 Large Scale Pilots	Diverse	Planning more virtual events
WP3 Harmonization & interoperability	Yet unclear, dependency on other WPs and activities	Planning more virtual events; focusing on some specific issues
WP4 Knowledge Information System	Minimum	Keep work going; execution phase
WP5 Innovation Ecosystem	Stakeholder forum meetings are not possible, adjustment needed	Exploring plans for virtual Stakeholder Forum meetings
WP6 Call for Subcontracting of Software Components & Pilot Validations	1-2 months delay due to non-availability of core staff	Now top priority to finalise first round

Thank you!

www.niva4cap.eu

T:@niva4cap

sander.janssen@wur.nl



This project has received funding from the European Union's Horizon 2020 research and innovation programme under grant agreement no. 842009
